


# Citywide Privacy Wall Construction

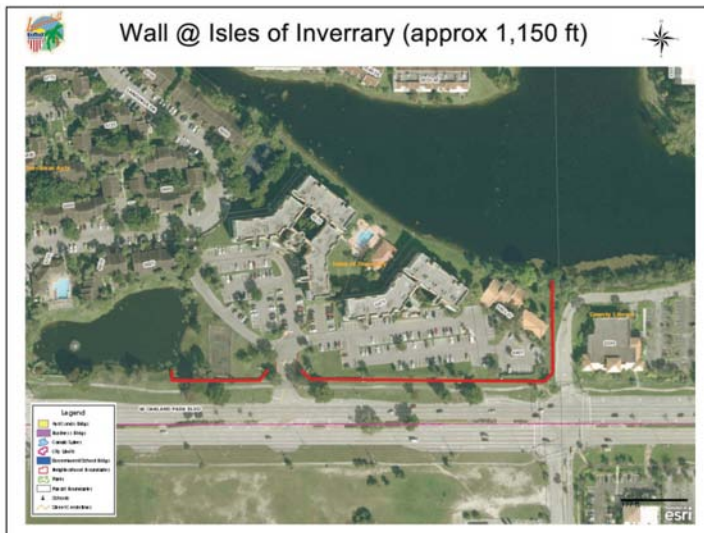

Planned location of Isles of Inverrary wall in red

Project Funding	Budget	Purchase		Expense	
		Orders	To Date	Balance	
Professional Services	\$ 200,000	\$ 2,050	0	\$ 197,950	
Construction	4,000,000	0	0	4,000,000	
Land Purchase	0	0	0	0	
Contingency	800,000	0	0	800,000	
<b>Totals</b>	<b>\$5,000,000</b>	<b>\$ 2,050</b>	<b>0</b>	<b>\$4,997,950</b>	

## Project Team:

Lead: Charlie Cuyler, Public Works Director

Tamica Dennis, Kennie Hobbs, Jr.

GO Management: J. Martin Cala, Buddy Shelton, Sean Henderson, Yolanda Todd, Don Giancoli, Doug Downs

The privacy walls installed as part of 2005 GO Bond were very attractive and popular with the community. The additional funding in 2016 will provide for three or four new areas, depending on final costs.

## Proposed Project Elements:

- New Walls at following locations
  - Isles of Inverrary – Oak Pk Blvd
  - NW 19 St west of NW 31 Ave
  - NW 19 St and NW 55-56 Ave
  - Remote water tank – Oak Pk Blvd
  - Golf Course north at NW 19 St
- Additional locations to be determined as funding allows

## Milestones

Design/Bid Plans	April, 2017
Bid Award	July, 2017
Construction Begins	September, 2017

## Project Status:

- ADA Engineering will submit cost proposal for design and bid docs for wall at Isles of Inverrary
- Purchase order issued to Avrom & Associates for survey

## Current Conditions



Existing wall at NW 19 St to be replaced at a future date
