


Citywide Privacy Wall Construction

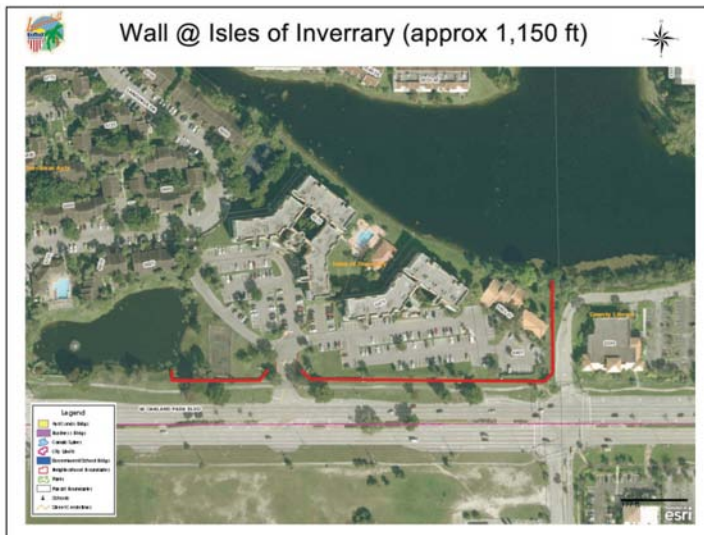

Planned location of Isles of Inverrary wall in red

Project	Budget	Purchase Orders	Expense To Date	Balance
Professional Services	\$ 200,000	\$ 2,050	0	\$ 197,950
Construction	4,000,000	0	0	4,000,000
Land Purchase	0	0	0	0
Contingency	800,000	0	0	800,000
Totals	\$5,000,000	\$ 2,050	0	\$4,997,950

Project Team:

Lead: Charlie Cuyler, Public Works Director

Tamica Dennis, Kennie Hobbs, Jr.

GO Management: J. Martin Cala, Buddy Shelton, Sean Henderson, Yolanda Todd, Don Giancoli, Doug Downs

The privacy walls installed as part of 2005 GO Bond were very attractive and popular with the community. The additional funding in 2016 will provide for three or four new areas, depending on final costs.

Proposed Project Elements:

- Phase 1 locations
 - Isles of Inverrary – Oak Pk Blvd
 - NW 19 St and NW 55-56 Ave
 - Remote water tank – Oak Pk Blvd
- Phase 2 locations
 - Golf Course north at NW 19 St
 - Enclave at Inverrary Blvd
 - NW 19 St west of NW 31 Ave
- Additional locations to be determined as funding allows

Milestones

Design/Bid Plans	June, 2017
Bid Award	August, 2017
Construction Begins	September, 2017

Project Status:

- ADA Engineering design proposal being reviewed by Project Team
- Survey completed for Isles of Inverrary by Avirom & Associates

Current Conditions



Existing wall at NW 19 St to be replaced at a future date
