



# John Mullin Park Improvements

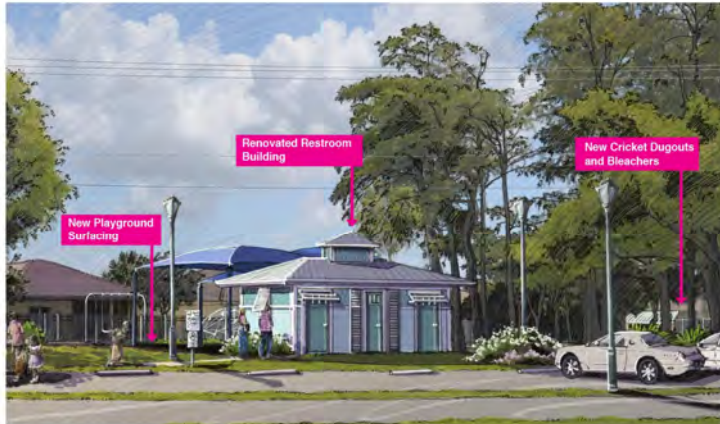

 John Mullin Park Restroom Building - After Park, Recreational, Leisure and Cultural Projects  
City of Lauderdale, Florida

## Proposed Project Elements:

- Basketball Courts renovation
- New Walking Path
- Renovate Baseball Fields and Dugouts
- Restroom Renovations
- Outdoor Play Equipment / Furniture

## Milestones

Conceptual Plan	January, 2017
Design/Bid Plans	May, 2017
Bid Award	August, 2017
Construction Begins	October, 2017

## Project Status:

- Project Team developing plans, cost estimates and bid documents for improvement options

Project Funding	Budget	Purchase		Expense To Date	Balance
		Orders			
Basketball Courts	\$ 190,000	0		0	\$ 190,000
Walking Path	250,000	0		0	250,000
Fields and Dugouts	60,000	0		0	60,000
Restroom Renovations	250,000	0		0	250,000
Outdoor Furniture	50,000	0		0	50,000
<b>Totals</b>	<b>\$ 800,000</b>	<b>0</b>		<b>0</b>	<b>\$ 800,000</b>

## Current Conditions



The restrooms at Mullin Park will be renovated as part of this project

## Project Team:

Lead: Scott Newton, Assistant Director, PALS

Irvin Kiffin, Brian Picinic, Vince Miller, Rhea Warner, Desorae Giles-Smith

GO Management: J. Martin Cala, Buddy Shelton, Sean Henderson, Yolanda Todd, Don Giancoli, Doug Downs

Improvements at John Mullin Park on NW 55<sup>th</sup> Street are designed to bring the entire park up to the standards of the new Pool and Community Center
