

Citywide Police Camera System



New poles for the cameras and license plate readers can be combined with solar panels for standalone operation

Proposed Project Elements:

- Cameras installed at City Parks, buildings and facilities, major intersections and entrances to City
- Data storage system at new Police Station


Milestones

Phase II Start	June, 2020
Training Complete	July, 2020
Project Complete	January, 2021

Project Status:

- Rekor Recognition awarded bid
- Total of 73 cameras / license plate readers, 90% installed to date
- Installed cameras have been used to collect evidence for arrests and stolen vehicle recovery

Current Conditions

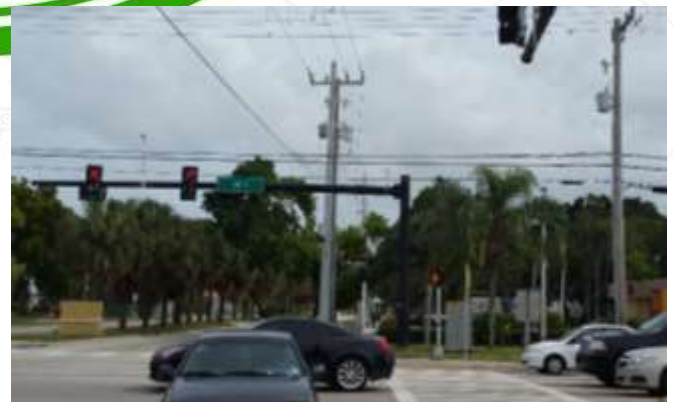

Most cameras will need to be mounted on new poles to avoid conflict with existing utilities and maximize views

Project Funding	Budget	Purchase Orders	Expense To Date	Balance
Professional Services	\$399,292	\$0	\$399,292	\$0
Construction	4,353,719	0	4,353,719	0
Contingency	0	0	0	0
Totals	\$4,753,011	\$0	\$4,753,011	\$0

Project Team:

Lead: Doug Downs, MIS Manager

Allen Siegel, Dave Hennessy, Kennie Hobbs, Jr.

The video surveillance system is designed to collect video evidence for criminal investigations but will not be monitored in real time.
